

Work Order ID 151108

Monday, September 12, 2016 10:34:01 AM

151108

Page 1

Item ID: D4149-1 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Crosstube Lug Plate, Aft
Start Date: 9/9/2016 Start Qty: 12.00 ***12*** Cust Item ID:
Required Date: 9/12/2016 Req'd Qty: 12.00 ***12*** Customer:

Reference:

DAS
21

Approvals: Process Plan: 9-89 Date SEP 14 2016 Tooling: Date: Run Start ***NR1***
QC: Date: SPC (Y/N): Date: Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
Draw Nbr	Revision Nbr								
D4149	C								

100

0.00

100

Waterjet

FLOW CNC Waterjet

Memo

Cut as per dwg D4149

Prog Rev: C

Dwg Rev: C

OPEN TO HOLES TO FINISH SIZE AS PER DWG

Deburr as required

0.28

(12)

09/16/10/09

110

QC2- Inspect parts off machine FAI/FAIB

0.00

110

QC

Quality Control

Memo

0.02

(12)

09/16/10/09

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : _____					

Work Order ID 151108

Monday, September 12, 2016 10:34:01 AM

151108

Item ID: D4149-1

Accept

N900040100

Setup Star

Revision ID:

Item Name: Crosstube Lug Plate, Aft

Stop

Start Date: 9/9/2016

Start Qty: 12.00

12

Cust Item ID:

Required Date: 9/12/2016

Req'd Qty: 12.00

12

Customer:

Reference:

Approvals:

Process Plan: _____

Date: _____

Tooling: _____

Date: _____

Run Star

QC: _____

Date: _____

SPC (Y/N): _____

Date: _____

Stop

Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
Qty

120

QC8- Inspect parts - second check

0.00

120

QC

Memo

0.04

Quality Control

OCT 11 2016

150

Identify as per dwg & Stock Location: Stock

0.00

150

Packaging

Memo

0.02

Packaging

OCT 12 2016

160

QC21- Final Inspection - Work Order Release

0.00

160

QC

Memo

0.20

Quality Control

OCT 12 2016

VS 16/10/12

DAS
21
9-89

OCT 12 2016

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐							
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval			
Description Work Order Deviation				Disposition							

Root Cause				FAULT CATEGORY							
Environment	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong	☐
Design	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions	☐
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance	☐
Equip/Tooling	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect	☐
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing	☐
Material	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved	☐
Internal Transport	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing	☐
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish	☐
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread	☐
Substation	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence	☐
Past Expiry Date	☐	Manufacturing Process	☐	OTHER : _____							
Misidentified	☐	Past Due	☐								

Picklist Print

Monday, September 12, 2016 10:34:00 AM

Page 1
1

Work Order ID: 151108

151108

Parent Item: D4149-1

D4149-1

Parent Item Name: Crosstube Lug Plate, Aft

Start Date: 9/9/2016

Required Date: 9/12/2016

Start Qty: 12.00

Required Qty: 12.00

Comments: IPP Rev:A 10.06.24 new issue DD verf:EC
IPP Rev:B 11.03.03 as per revC DD verf:JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
M304S11GA		Purchased		No		100	sf	70.1100	0.1355	1.711579			

M304S11GA

304/316 0.125 Sheet

DE 10/10/09

Location

Loc Qty

Loc Code

MAT020

70.10998

M129545

2.21998

M129972

0.5

M134284

2.79

M135355

64.6

1.8

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐
OTHER :					


DART AEROSPACE LTD		Work Order:	151108
Description: Aft Crosstube Lug Plate		Part Number:	D4149-1
Inspection Dwg: D4149 Rev: C		Page 1 of 1	

FIRST ARTICLE INSPECTION CHECKLIST

Drawing Dimension	Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
Ø0.129	+0.005/-0.001	Ø.130	/		V: D-02	
Ø0.191	+0.005/-0.001	Ø.192	/			
Ø0.257	+0.006/-0.001	Ø.258	/			
Ø0.38	+0.006/-0.001	Ø.379	/			
0.380	+/-0.010	.386	/			
0.469	+/-0.010	.471	/			
0.310	+/-0.010	.313	/			
0.750	+0.005/-0.010	.751	/			
3.25	+/-0.030	3.25	/			
0.65	+/-0.030	.65	/			
0.63	+/-0.030	.63	/			
5.46	+/-0.030	5.46	/			
3.80	+/-0.030	3.80	/			
2.13	+/-0.030	2.13	/			
1.313	+/-0.010	1.315	/			
0.625	+/-0.010	.627	/			
0.375	+/-0.010	.379	/			
1.175	+/-0.010	1.178	/			
0.752	+/-0.010	.755	/			
1.588	+/-0.010	1.589	/			
1.587	+/-0.010	1.588	/			
11.15	+/-0.030	11.15	/			
0.750	+/-0.010	.759	/			
1.55	+/-0.030	1.55	/			
1.12	+/-0.030	1.12	/			
8.42	+/-0.030	8.42	/			
2.70	+/-0.030	2.70	/			
0.125	+/-0.010	.116	/			
Ø0.252	+0.003/-0.000	Ø.253	/			

Measured by:	DC	Audited by:	DAS 38 9-89	Preliminary Approval:	
Date:	16/10/09	Date:	OCT 11 2016	Date:	

Rev	Date	Change	Revised by	Approved
A	10.08.04	New Issue	KJ	
B	12.02.01	Dimensions updated per Dwg Rev C	KJ	

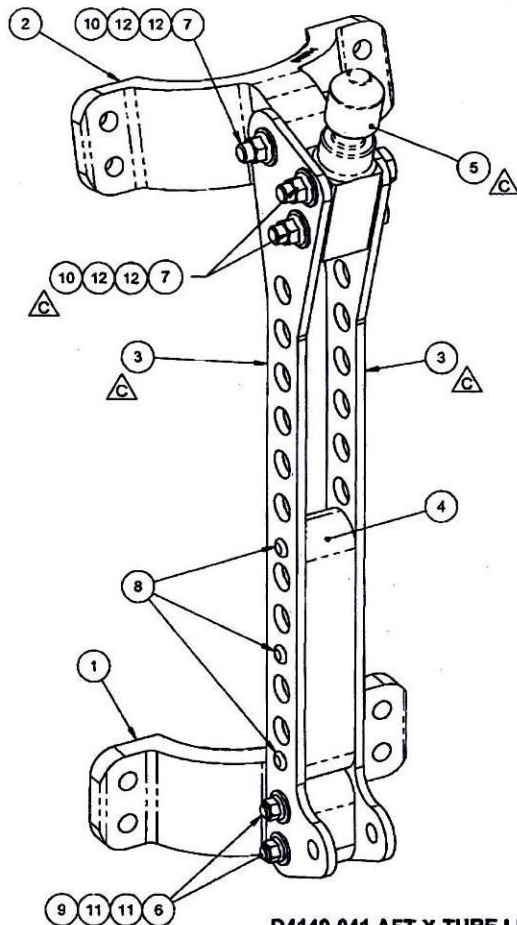

D4149-041 AFT X-TUBE LUG ASSY

NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: IDENTIFY WITH DART P/N "D4149-041" USING FINE POINT PERMANENT INK MARKER
- 7) WEIGHT: 2.21 lbs

ITEM	QTY -041	P/N	DESCRIPTION
	X	D4149-041	AFT X-TUBE LUG ASSY
1	1	D3910-1	X-TUBE LUG
2	1	D4091-1	MOUNTING LUG
3	2	D4149-1	AFT X-TUBE LUG PLATE
4	1	D4149-3	SPACER
5	1	D4149-5	EYEBOLT STUD
6	2	AN3C12A	BOLT
7	3	AN4C13A	BOLT
8	3	MS20615-4M18	RIVET
9	2	MS21043C3	NUT
10	3	MS21043C4	NUT
11	4	NAS1149C0332R	WASHER
12	6	NAS1149C0432R	WASHER

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER


NO 151108 MJS

16-09-14

RELEASED
2011-02-24

C	HOLE DIA CHANGED TO 0.252" (D8-3); HOLE DIA CHANGED TO 0.250" (C8-5); REPLACED QTY(2) AN3C12A, MS21043C3 AND QTY(4) NAS1149C0332R WITH QTY(2) AN4C13A, MS21043C4 AND QTY(4) NAS1149C0432R (D3-1, D7-2)	SC	11.02.22
B	MS20615-4M18 WAS MS20615-4M20 (ZN D3-1 & B7-2); ADDED D4149-5 (SHT 5); D4149-5 WAS D3909-5 (ZN D3-1 & D7-2); REPLACED QTY(3) MS20615-4M18 WITH QTY(2) EACH AN3C12A, MS21043-3 AND QTY(4) NAS1149C0332R WASHER (ZN D3-1, C7-1, B7-2 & B3-2); Ø.0191 2 PL REPLACES Ø.0129 3 PL (ZN D8-3). REASON: SEE TR-D350-007-2 REV. B.	MB	10.07.05
A	NEW ISSUE	MB	10.06.18
REV.	DESCRIPTION	BY	DATE
DESIGN	MB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	SC		
CHECKED		DRAWING NO.	REV. C
MFG. APPR.		D4149	SHEET 1 OF 5
APPROVED		TITLE	SCALE
DE APPR.		AFT X-TUBE LUG ASSY	NTS
DATE	11.02.22	COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL, AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	


8 7 6 5 4 3 2 1


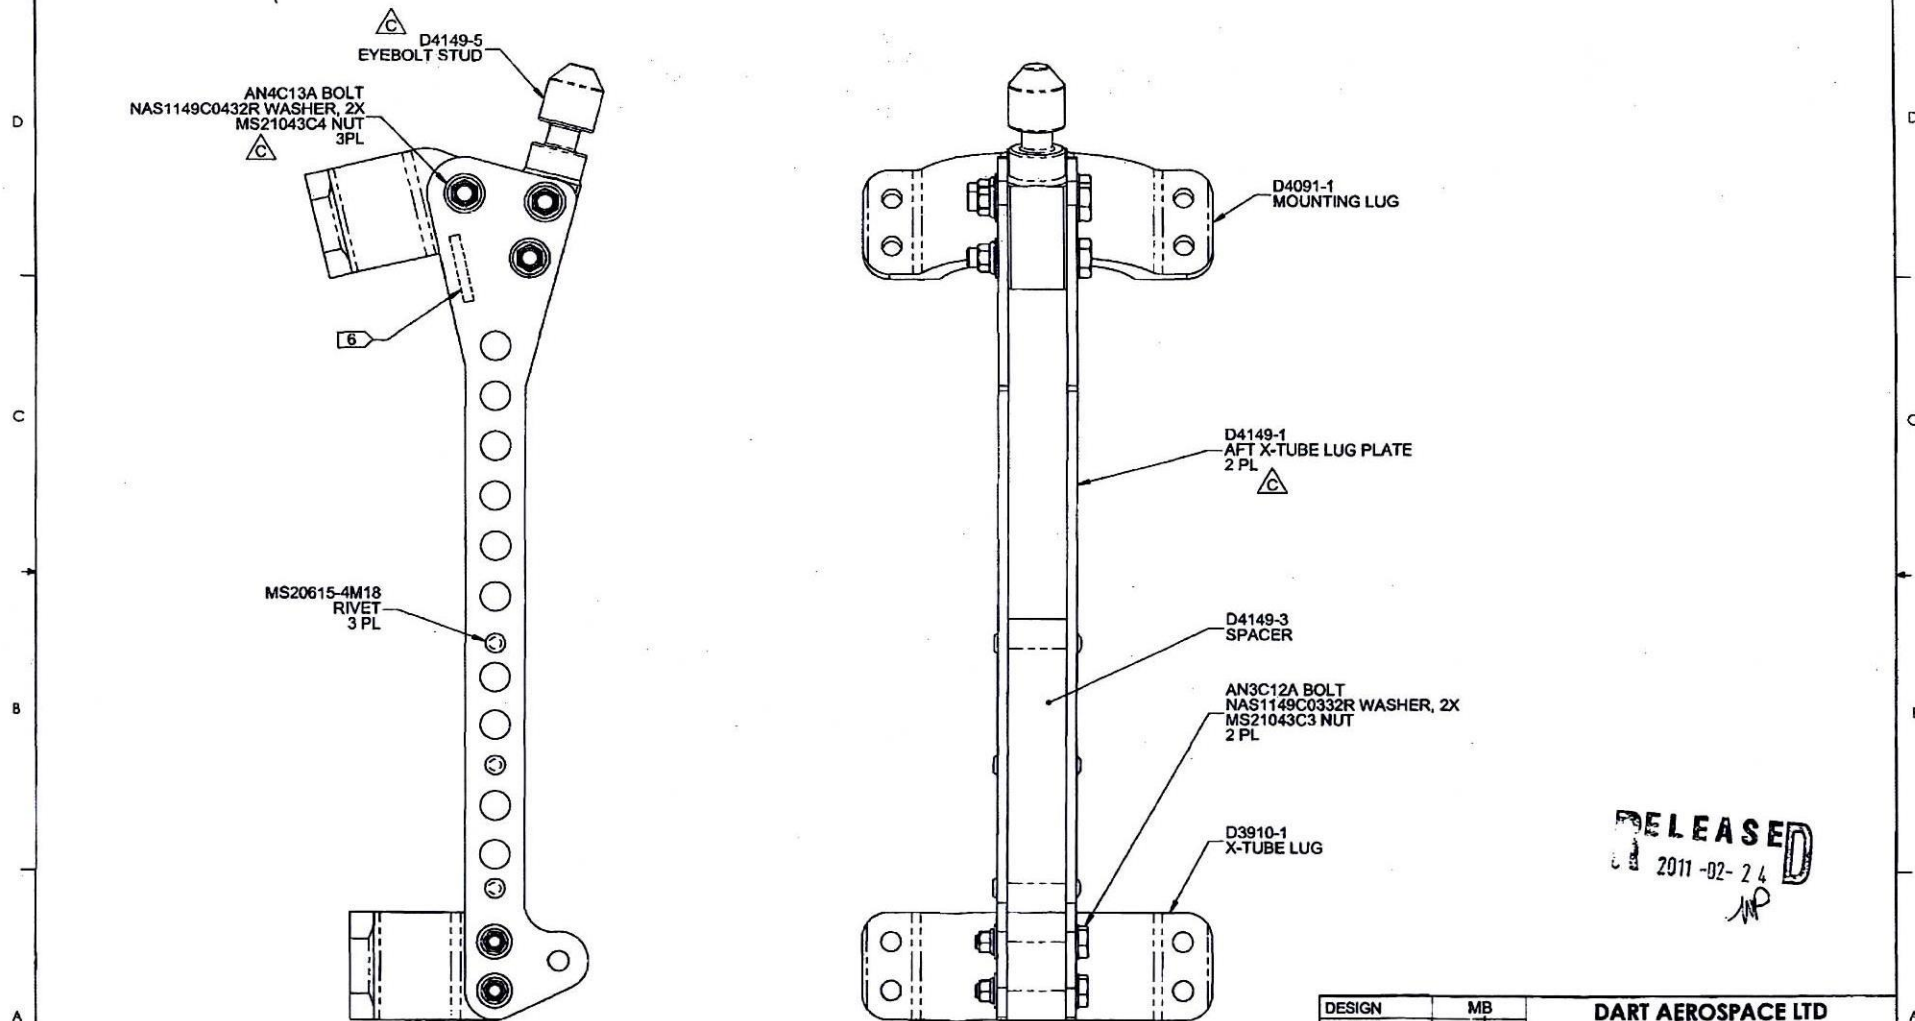


D4149-041 AFT X-TUBE LUG ASSY


DESIGN	MB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	SC		
CHECKED		DRAWING NO.	REV. C
MFG. APPR.		D4149	SHEET 2 OF 5
APPROVED		TITLE	SCALE
DE APPR.		AFT X-TUBE LUG ASSY	NTS
DATE	11.02.22	COPYRIGHT © 2019 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

8 7 6 5 4 3 2 1

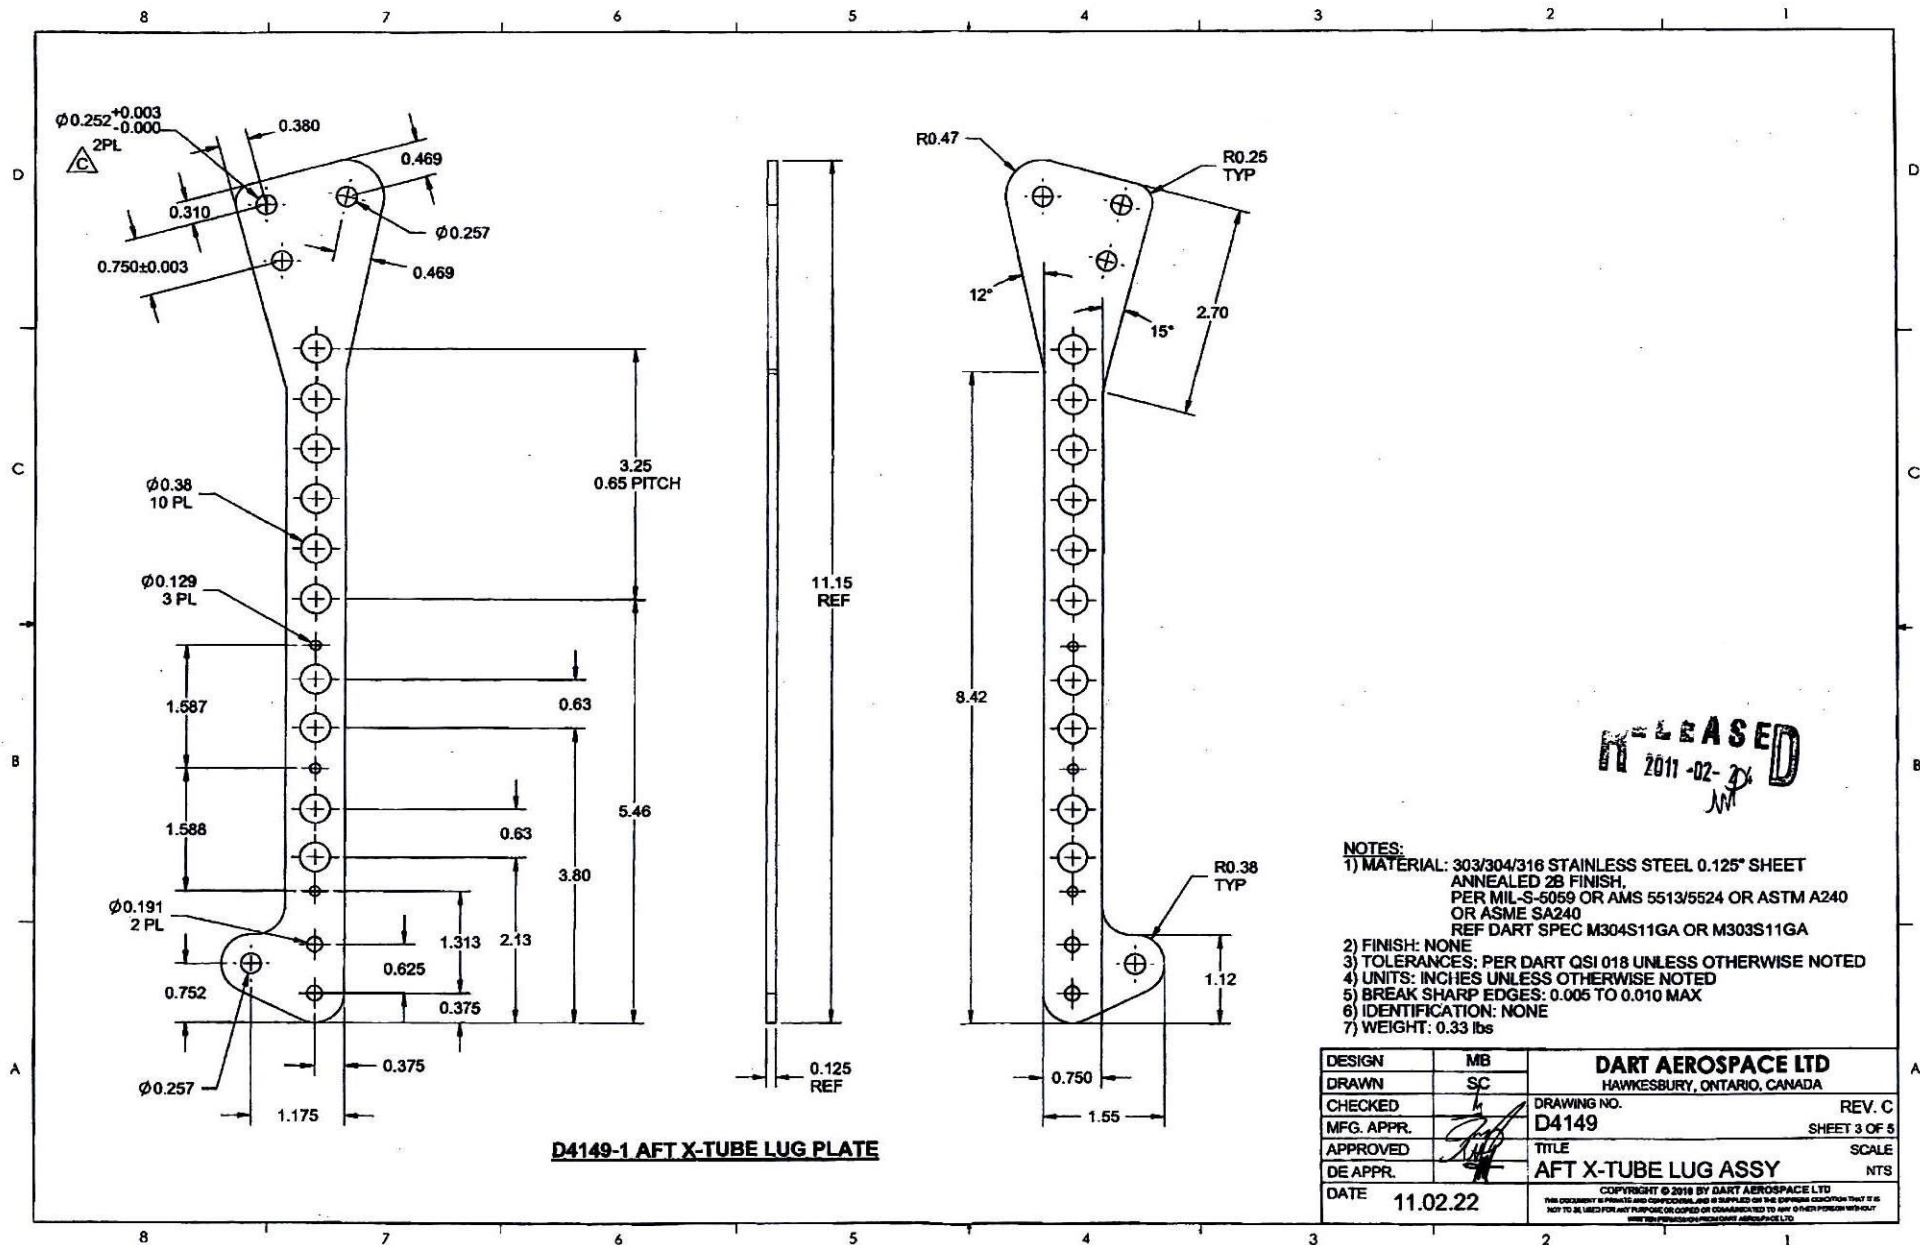

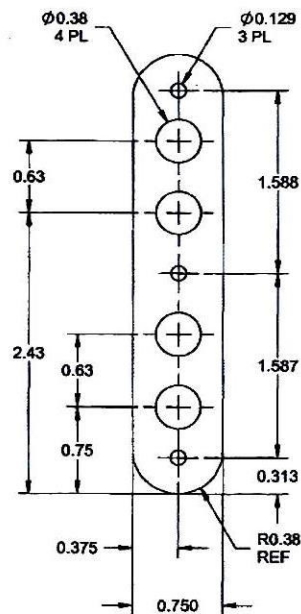

D4149-3 SPACER





NOTES:

- 1) MATERIAL: 303/304/316 STAINLESS STEEL BAR PER ASTM A276 OR A582
REF DART SPEC MS304B OR MS303B
- 2) FINISH: NONE
- 3) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK ALL SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.47 lbs

DESIGN	MB	DART AEROSPACE LTD	
DRAWN	SC	HAWKESBURY, ONTARIO, CANADA	
CHECKED		DRAWING NO.	REV. C
MFG. APPR.		D4149	SHEET 4 OF 5
APPROVED		TITLE	SCALE
DE APPR.		AFT X-TUBE LUG ASSY	NTS
DATE	11.02.22	COPYRIGHT © 2010 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL, AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR LOANED OR COMMENCED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			

RELEASED
2011-02-24

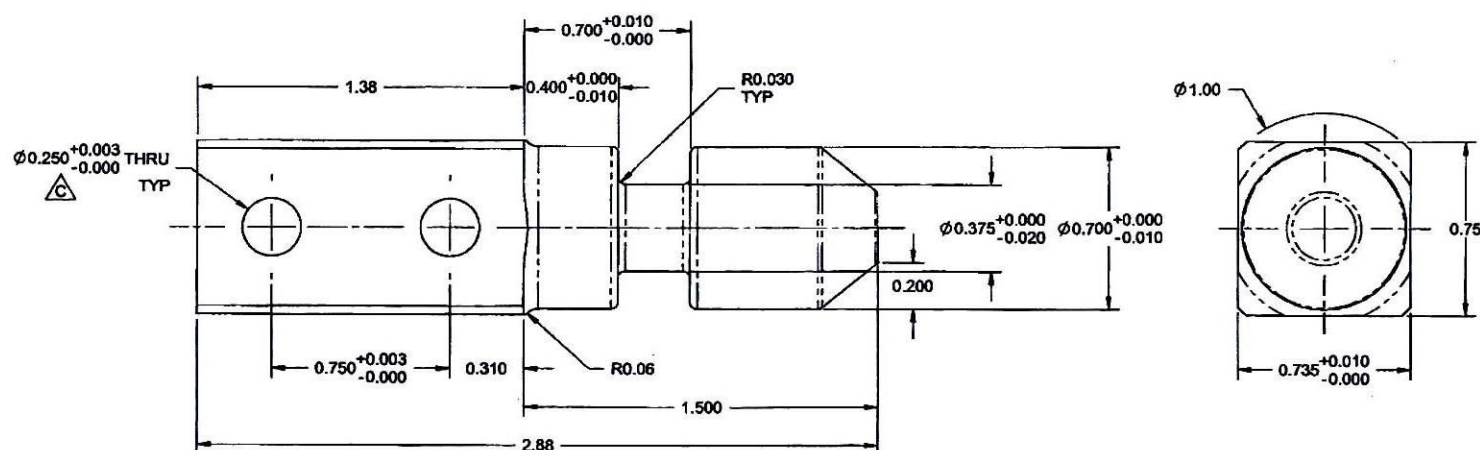

D4149-5 EYEBOLT STUD

RELEASED
2011-02-24

NOTES:

- 1) MATERIAL: 303/304/316 STAINLESS STEEL BAR PER ASTM A276 OR A582
REF DART SPEC MS304B OR MS303B
- 2) FINISH: NONE
- 3) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK ALL SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: IDENTIFY WITH DART P/N "D4149-5" USING FINE POINT PERMANENT INK MARKER
- 7) WEIGHT: 0.32 lbs

DESIGN	MB	DART AEROSPACE LTD	
DRAWN	SC	HAWKESBURY, ONTARIO, CANADA	
CHECKED		DRAWING NO.	REV. C
MFG. APPR.		D4149	SHEET 5 OF 5
APPROVED		TITLE	SCALE
DE APPR.		AFT X-TUBE LUG ASSY	NTS
DATE	11.02.22	COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS UNDERSTANDING THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD	
